




# PERCHLOROETHYLENE DRY CLEANERS



## COMPLIANCE INSPECTION CHECKLIST

**INSPECTION TYPE:** ANNUAL (INS1, INS2)  COMPLAINT/DISCOVERY (CI)   
 RE-INSPECTION (FUI)  ARMS COMPLAINT NO: \_\_\_\_\_

<b>AIRS ID#:</b> 103 0296	<b>Date:</b> 3/26/2009	<b>Time In:</b> 1:20PM	<b>Time Out:</b> 1:50PM
<b>Facility Name:</b>	Spartan Enterprises, Inc.		
<b>Facility Location:</b>	32646 U.S. Highway 19 North Palm Harbor, FL, 34684		
<b>Responsible Official:</b>	Keith McNamara	<b>Phone No:</b>	727-784-4050
<b>Emis. Unit Description:</b>	New, Large Perchloroethylene Dry Cleaner. One Dry-to-dry machine, purchased in December 1994, with a refrigerated condenser. 25 HP, natural gas fired boiler is on-site.		
<b>Permit Number:</b>	1030296-003-AG	<b>Exp. Date:</b>	7/26/11
<b>Facility Contact:</b>	Keith McNamara	<b>Phone:</b>	727-784-4050
<b>Compliance Status:</b>	<input checked="" type="checkbox"/> IN <input type="checkbox"/> MNC <input type="checkbox"/> SNC		

### PART I: NOTIFICATION (Check appropriate box)

- Existing facility notified DARM by 9/1/96
- New facility notified DARM 30 days prior to startup
- Facility failed to notify DARM to use general permit

### PART II: CLASSIFICATION

Facility indicated on notification form that it is:

- No Notification Form     Drop-Off Store     Out of business     Petroleum Solvent Only

- A.**
- |   |  |
|---|--|
| <u>1. Existing small area source</u><br>Dry-to-dry only, x <140 gal/yr<br>Transfer only, x <200 gal/yr <input type="checkbox"/><br>Both types, x <140 gal/yr<br>(Constructed before 12/9/91)                      | <u>2. New small area source</u><br>Dry-to-dry only, x <140 gal/yr<br>Transfer only, x <200 gal/yr <input type="checkbox"/><br>Both types, x <140 gal/yr<br>(Constructed on or after 12/9/91)                                 |
| <u>3. Existing large area source</u><br>Dry-to-dry only, 140> x <2,100 gal/yr<br>Transfer only, 200> x <1,800 gal/yr <input type="checkbox"/><br>Both types, 140> x <1,800 gal/yr<br>(Constructed before 12/9/91) | <u>4. New large area source</u><br>Dry-to-dry only, 140> x <2,100 gal/yr<br>Transfer only, 200> x <1,800 gal/yr <input checked="" type="checkbox"/><br>Both types, 140> x <1,800 gal/yr<br>(Constructed on or after 12/9/91) |

This is a correct facility classification  Y  N  Can not determine

If no, please check the appropriate classification:

facility qualified for a general permit as number 4 above.

facility exceeds above limits and is not eligible for a general permit

**B. Highest 12-month consecutive total of perchloroethylene purchased in the preceding 12-month period:** 120 Gallons, in October 2008, as of 2/2009 = 90 gallons.

### PART III: GENERAL CONTROL REQUIREMENTS

Is the responsible official of the dry cleaning facility: (Check appropriate boxes)

- |   |                                       |                            |  |
|---|---------------------------------------|----------------------------|--|
| 1. Storing perchloroethylene in tightly sealed and impervious containers?   | <input checked="" type="checkbox"/> Y | <input type="checkbox"/> N | <input type="checkbox"/> NA            |
| 2. Examining the containers for leakage?  | <input checked="" type="checkbox"/> Y | <input type="checkbox"/> N | <input type="checkbox"/> NA            |
| 3. Closing and securing machine doors except during loading/unloading?  | <input checked="" type="checkbox"/> Y | <input type="checkbox"/> N |  |
| 4. Draining cartridge filters in their housing or in sealed containers for at least 24 hours prior to disposal?                     | <input checked="" type="checkbox"/> Y | <input type="checkbox"/> N | <input type="checkbox"/> NA            |
| 5. Maintaining solvent-to-carbon ratios and steam pressure for carbon adsorber beds according to the manufacturer's specifications? | <input type="checkbox"/> Y            | <input type="checkbox"/> N | <input checked="" type="checkbox"/> NA |

### PART IV: PROCESS VENT CONTROLS

#### **In Part II-A:**

If classification (1) has been checked, no controls are required. **Proceed to Part V.**

If classification (2) has been checked, the machine should be equipped with a refrigerated condenser (complete A below)

If classification (3) has been checked, the machine should be equipped with either a refrigerated condenser or a carbon adsorber (complete A and B below). A Carbon adsorber must have been installed prior to September 22, 1993.

**If classification (4) has been checked, machine should be equipped with a refrigerated condenser (complete A and B below.)**

#### **A. Has the responsible official of all new sources and existing large area sources:** (check appropriate boxes)

- |  |                                       |                            |                             |
|--|---------------------------------------|----------------------------|-----------------------------|
| 1. Equipped all machines with the appropriate vent controls?   | <input checked="" type="checkbox"/> Y | <input type="checkbox"/> N |                             |
| 2. Equipped dry-to-dry machines with a closed-loop vapor venting system?   | <input checked="" type="checkbox"/> Y | <input type="checkbox"/> N | <input type="checkbox"/> NA |
| 3. Equipped the condenser with a diverter valve so airflow will be directed away from the condenser upon opening the door?                 | <input checked="" type="checkbox"/> Y | <input type="checkbox"/> N | <input type="checkbox"/> NA |
| 4. Measured and recorded the temperature of the outlet exhaust stream of a refrigerated condenser on a weekly basis?                       | <input checked="" type="checkbox"/> Y | <input type="checkbox"/> N |                             |
| 5. Repaired or adjusted the equipment within 24 hours if the exhaust temperature of the condenser exceeded 45o F?                          | <input checked="" type="checkbox"/> Y | <input type="checkbox"/> N | <input type="checkbox"/> NA |
| 6. Conducted all temperature monitoring after an appropriate cool down period and after verifying the coolant had been completely charged? | <input checked="" type="checkbox"/> Y | <input type="checkbox"/> N |                             |

**B. Has the responsible official of an existing large or new large area source also:**

- |  |  |
|--|--|
| 1. Measured and recorded the exhaust temperature on the outlet side of the condenser located on dry-to-dry, reclaimer, and dryer machines on a weekly basis?   | <input checked="" type="checkbox"/> Y <input type="checkbox"/> N   |
| 2. Measured and recorded the washer exhaust temperature at the condenser inlet and outlet weekly?<br>Is the temperature differential equal to or greater than 10°F?  | <input type="checkbox"/> Y <input type="checkbox"/> N <input type="checkbox"/> NA<br><input type="checkbox"/> Y <input type="checkbox"/> N <input type="checkbox"/> NA |
| 3. Measured and recorded the perc concentration weekly at the end of the final drying cycle while the machine is venting to the atmosphere. If machines are equipped with a carbon adsorber?<br>Is the perc concentration or less than 10 ppm?   | <input type="checkbox"/> Y <input type="checkbox"/> N <input type="checkbox"/> NA<br><input type="checkbox"/> Y <input type="checkbox"/> N <input type="checkbox"/> NA |
| 4. Assured that the sampling position on adsorber exhaust for measuring perc. concentrations is at least 10 duct diameters downstream of any bend, contraction, or expansion; is at least 10 diameters upstream from any bend contraction, or expansion; and downstream from the adsorber inlet? | <input type="checkbox"/> Y <input type="checkbox"/> N <input type="checkbox"/> NA  |
| 5. Equipped transfer machines (dryers, reclaimers, and washers) with individual condenser coils?   | <input type="checkbox"/> Y <input type="checkbox"/> N <input type="checkbox"/> NA  |
| 6. Routed airflow to the carbon adsorber (if used) at all times?   | <input type="checkbox"/> Y <input type="checkbox"/> N <input type="checkbox"/> NA  |

**PART V: RECORDKEEPING REQUIREMENTS**

**Has the responsible official:**

(Check appropriate boxes)

- |  |  |
|--|--|
| 1. Maintained receipts for perc purchased?   | <input checked="" type="checkbox"/> Y <input type="checkbox"/> N                             |
| 2. Maintained rolling monthly averages of perc consumption?  | <input checked="" type="checkbox"/> Y <input type="checkbox"/> N                             |
| 3. Maintained leak detection inspection and repair reports for the following:  |  |
| a. Documentation of leaks repaired w/in 24 hrs? or;  | <input type="checkbox"/> Y <input type="checkbox"/> N <input checked="" type="checkbox"/> NA |
| b. Documentation of parts ordered to repair leak and leak repaired w/in 2 days and parts installed w/in 5 days of receipt? | <input type="checkbox"/> Y <input type="checkbox"/> N <input checked="" type="checkbox"/> NA |
| 4. Maintained calibration data? ( <i>direct reading instruments only</i> )   | <input type="checkbox"/> Y <input type="checkbox"/> N <input checked="" type="checkbox"/> NA |
| 5. Maintained exhaust duct monitoring data on perc concentrations?   | <input type="checkbox"/> Y <input type="checkbox"/> N <input checked="" type="checkbox"/> NA |
| 6. Maintained startup/shutdown/malfunction plan?   | <input checked="" type="checkbox"/> Y <input type="checkbox"/> N                             |
| 7. Maintained deviation reports?   | <input type="checkbox"/> Y <input checked="" type="checkbox"/> N <input type="checkbox"/> NA |
| Problem corrected?   | <input type="checkbox"/> Y <input checked="" type="checkbox"/> N <input type="checkbox"/> NA |
| 8. Maintained compliance plan, if applicable?  | <input type="checkbox"/> Y <input type="checkbox"/> N <input checked="" type="checkbox"/> NA |

**PART VI: LEAK DETECTION AND REPAIRS**

<b>1. Does the responsible official conduct a weekly leak detection and repair inspection?</b>	<input checked="" type="checkbox"/> Y	<input type="checkbox"/> N
<b>2. Which method of detection does the responsible official use?</b>	<input checked="" type="checkbox"/> Y	<input type="checkbox"/> N
Visual examination (condensed solvent of exterior surfaces)	<input checked="" type="checkbox"/>	
Physical detection (airflow felt through gaskets)	<input checked="" type="checkbox"/>	
Odor (noticeable perc odor)	<input checked="" type="checkbox"/>	
Use of direct-reading instrumentation (FID/PID/calorimetric tubes)	<input type="checkbox"/>	
<b>If using direct-reading instrumentation, is the equipment:</b>	<input type="checkbox"/> Y	<input type="checkbox"/> N
a. Capable of detecting perc vapor concentrations in a range of 0-500 ppm	<input type="checkbox"/> Y	<input type="checkbox"/> N
b. Calibrated against a standard gas prior to and after each use (PID/FID only).	<input type="checkbox"/> Y	<input type="checkbox"/> N
c. Inspected for leaks and obvious signs of wear on a weekly basis?	<input type="checkbox"/> Y	<input type="checkbox"/> N
d. Kept in a clean and secure area when not in use.	<input type="checkbox"/> Y	<input type="checkbox"/> N
e. Verified for accuracy by use of duplicate samples (calorimetric only)?	<input type="checkbox"/> Y	<input type="checkbox"/> N
<b>3. Has the facility maintained a leak log?</b>	<input checked="" type="checkbox"/> Y	<input type="checkbox"/> N
<b>4. The following area should be checked for leaks by the inspector:</b>	<input checked="" type="checkbox"/> Y	<input type="checkbox"/> N
Hose connections, fitting couplings, and valves	<input checked="" type="checkbox"/> Y	<input type="checkbox"/> N
Door gaskets and seating	<input checked="" type="checkbox"/> Y	<input type="checkbox"/> N
Filter gaskets and seating	<input checked="" type="checkbox"/> Y	<input type="checkbox"/> N
Pumps	<input checked="" type="checkbox"/> Y	<input type="checkbox"/> N
Solvent tanks and containers	<input checked="" type="checkbox"/> Y	<input type="checkbox"/> N
Water separators	<input type="checkbox"/> Y	<input type="checkbox"/> N
Muck cookers	<input type="checkbox"/> Y	<input checked="" type="checkbox"/> N
Stills	<input checked="" type="checkbox"/> Y	<input type="checkbox"/> N
Exhaust dampers	<input checked="" type="checkbox"/> Y	<input type="checkbox"/> N
Diverter valves	<input type="checkbox"/> Y	<input checked="" type="checkbox"/> N
Cartridge Filter housing	<input checked="" type="checkbox"/> Y	<input type="checkbox"/> N

Shea Jackson	3/26/2009
Inspector=s Name (Please Print)	Date of Inspection
	Within one year of this inspection
Inspector=s Signature	Date of Next Inspection

## System Inspection and Leak Detection

Are the following dry cleaning system components inspected weekly for perceptible leaks (sight, smell or touch) while the system is in operation (§63.322(k))? (Inspection with a halogenated hydrocarbon detector or PCE gas analyzer also fulfills the requirement for inspection of perceptible leaks.) Y N NA

Are the following dry cleaning system components inspected monthly for vapor leaks using a halogenated hydrocarbon detector or PCE gas analyzer while the system is in operation? (Any inspection conducted according to this paragraph shall satisfy the requirements to conduct an inspection for perceptible leaks under §63.322(k) or (l).) Y N NA

- (1) Hose and pipe connections, fittings, couplings, and valves;
- (2) Door gaskets and seatings;
- (3) Filter gaskets and seatings;
- (4) Pumps;
- (5) Solvent tanks and containers;
- (6) Water separators;
- (7) Muck cookers;
- (8) Stills;
- (9) Exhaust dampers;
- (10) Diverter valves; and
- (11) All Filter housings

Is the halogenated hydrocarbon detector or PCE gas analyzer operated according to the manufacturer's instructions? Y N NA

**Comment:** *The Halogen detector alarm used to check for Perc leak. The facility is now following manufacturer's instructions by maintaining charged batteries.*

Is the vapor leak inspection conducted by placing the probe inlet at the surface of each component interface where leakage could occur and moving it slowly along the interface periphery? Y N NA

**Comment:** *This could not be determined at this time, the facility operator did not demonstrate use, and I found Perc leak with the detector during inspection.*

Is the PCE gas analyzer a flame ionization detector, photo ionization detector, or infrared analyzer capable of detecting vapor concentrations of PCE of 25 parts per million by volume? Y N NA

Is the halogenated hydrocarbon detector capable of detecting vapor concentrations of PCE of 25 parts per million by volume and indicating a concentration of 25 parts per million by volume or greater by emitting an audible or visual signal that varies as the concentration changes? Y N NA

**Comment:** *The facility has a halogenated detector model that was listed on the FDEP approved list, as capable of detecting 25 ppm*

## ADDITIONAL SITE INFORMATION

**Facility Name:** Spartan Enterprises, Inc.

**ARMS #:** 103 0296

- *I went to the facility to perform a re-inspection for the repairs of equipment which had previous been found to have a Perc leak.*
- *I met with Mr. Keith McNamara, the responsible official and we rechecked the dry to dry equipment.*
- *There were no perc odors detected around the machine during the inspection.*
- *Mr. McNamara used the facilities leak detector to perform leak check.*
- *It maintained an audible beep and did not alarm when the rear area of the machine near a Perc site window, and pipe fitting, which had previous been found to be leaking. (See photo).*
- *I informed Mr. McNamara that it appears the Perc leak had been corrected within 24 hours.*
- *A violation status had been assigned to this facility for failure to operate the halogen detector according to mfg instructions to detect the Perc leak. Tthe detector was now operating correctly.*
- *This facility appears to be in compliance at time of inspection.*

**ADDITIONAL SITE INFORMATION**

<b>Facility Name:</b>	Spartan Enterprises, Inc.
<b>ARMS #:</b>	103 0296

<b>Machine #1:</b>			
Manufacturer	Union	Capacity	lbs
Model#		Serial#	Mfg yr
<b>Machine #2:</b>			
Manufacturer		Capacity	lbs
Model#		Serial#	Mfg yr

**Notification (unpermitted sources only):**

- 1. Was the facility assisted in filling out the notification by the inspector?  Y  N
- 2. Did the facility insist on filling out its own notification, and will send it to FDEP?  Y  N

**Record keeping :**

- 1. Does facility have statement/specs as to the design accuracy of the temperature sensor?  Y  N  
 (Temperature of 45EF w/accuracy ∇2EF, or 7.2EC w/accuracy of ∇1.1EC)

**Hazardous Waste:**

- 1. Is all perc. contaminated wastewater either treated or disposed of properly?  Y  N
- 2. If wastewater is evaporated, is it an approved system, and using carbon filtration?  Y  N
- 3. Does the facility have secondary containment for the dry-dry machine?  Y  N
- 4. Does the facility have secondary containment for any perc. waste containers?  Y  N

**Boiler:**

Manufacturer	Hurst	Hp	25
Model #	4VTD25\50	Serial #	VGI-150-1233
		Mfg yr	2002

Fuel Type:    Natural gas?                          Propane?                        Fuel oil?           

**Comments:**    Boiler is exempt from permitting

## ENFORCEMENT SUMMARY

<b>Facility Name:</b>	Spartan Enterprises, Inc.
<b>ARMS #:</b>	103 0296


Viol#	Violation Description	Frequency	From	To
per00	Failure to notify and obtain a permit			
per01	No purchase records	Monthly		
per02	No perc. purchase rolling totals	Monthly		
per03	No leak log	<input type="checkbox"/> Weekly <input type="checkbox"/> Bi-weekly		
per04	No temp. log	Weekly		
per05	No SSM plan			
per06	Temp. sensor accuracy verification			
per07	No leak checks	<input type="checkbox"/> Weekly <input type="checkbox"/> Bi-weekly		
per08	No temp. checks	Weekly		
per09	Perceptible leaks			
per10	No carbon absorber			
per11	No carbon absorber test	Weekly		
per12	No leak tight containers			
per13	No separator pre-filter			
per14	Leaks not repaired within 24hrs.			
per15	Repair refrig. cond./carbon abs. within 2 days			

Viol#	Comments
	The Halogen Detector appears to be operated according to manufacturer's directions.



# Spartan Enterprises, Inc. Spartan Cleaners - Plant #1

32646 U.S. Highway 19 North, Palm Harbor

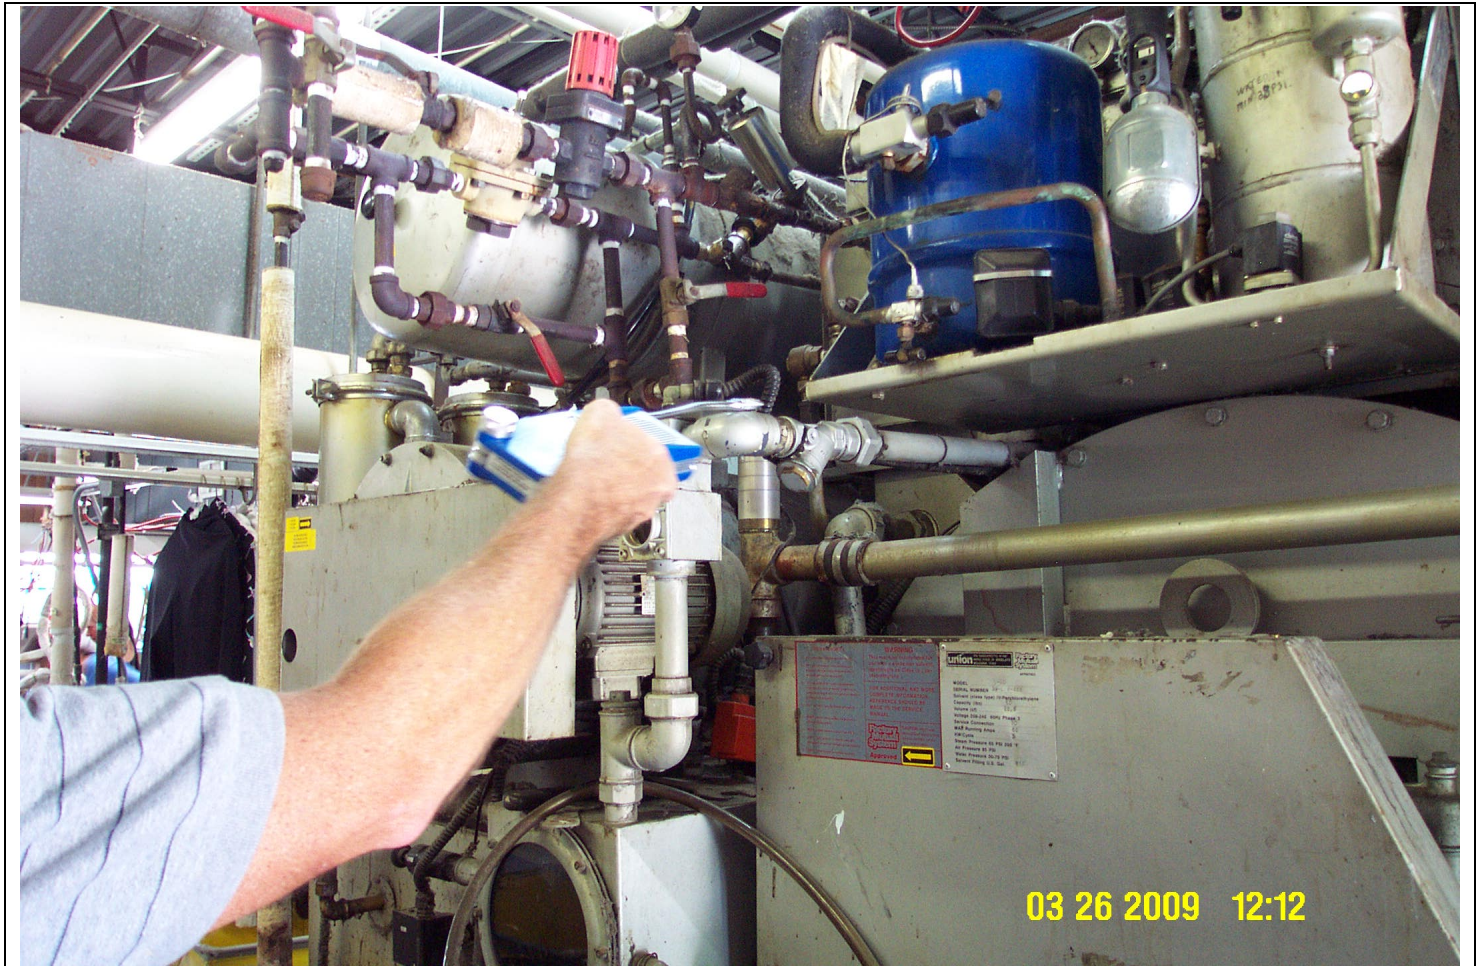

**Project Id:** 66967      **Permit No:** 1030296-003-AG      **Arms Number:** 0296

**Inspector:** Shea Jackson      **Inspection Date:** 2/23/09

**Source (EU):** New, Large Perchloroethylene Dry Cleaner. One Dry-to-dry machine, purchased in December 1994, with a refrigerated condenser. 25 HP, natural gas fired boiler is on-site

**Description:** [The facilities Halogen detector in use by the facility RO, Mr. McNamara showed the Perc leak had been corrected.]
